



Module Code	:	CT050-3-3-PRMGT
Intake Code	:	APD3F2601CS(CYB)
Lecturer Name	:	TS. JERRY CHONG CHEAN FUH
Hand in Date	:	26 TH APRIL 2026
Tutorial No.	:	T-2
Group No.	:	G4
Group Leader	:	GURSHAREENJIT KAUR A/P KARAMJIT SINGH

Student ID	Student Name
TP070385	GURSHAREENJIT KAUR A/P KARAMJIT SINGH
TP070844	HEMANTHRAJAH A/L KRISHNARAJAH
TP071154	ANUSHA DEVY A/P BRAHMATARAN
TP070071	DARMIK ISHWAR
TP071194	ADAM JEROME JOSEPH
TP070996	SAILESS RAJ A/L RAJENDRAN
TP070635	DARSYEN S/O GUNASEGARAN
TP071046	THOVINNASH A/L RAMESH
TP078596	AHMED ABDULHAMEED SALEH EZZALDEEN

Table of Contents

1.0 SUMMARY LEVEL DESCRIPTION OF THE PROJECT	3
2.0 SCOPE, OBJECTIVES AND COMPLETION CRITERIA	3
2.1 PROJECT OBJECTIVES.....	3
2.2 ACCEPTANCE CRITERIA.....	5
2.3 EVIDENCE OF COMPLETION.....	13
3.0 EVALUATION OF QUALITY OBJECTIVE	15
3.1 QUALITY OBJECTIVES	15
3.2 PROJECT AND PRODUCT QUALITY CRITERIA	16
4.0 SCHEDULE OBJECTIVES	22
5.0 SUMMARY OF FINAL PROJECT	23
6.0 SUMMARY OF RISKS AND ISSUES.....	24
7.0 LESSONS LEARNED SUMMARY	26
8.0 PROJECT ASSESSMENT	26
9.0 APPENDIX	28
PRMGT PROJECT PLAN	28
SCOPE	29
PROJECT SCHEDULE AND GANTT CHART	30
WORKLOAD MATRIX.....	31
WORK BREAKDOWN STRUCTURE.....	33
RISK REGISTER	34
QUALITY MATRIX.....	36

1.0 Summary Level Description of The Project

The GrowTogether initiative was a 14-week learning-oriented project designed and implemented by nine individuals trying to create awareness about the potential for utilizing urban space for promoting food sustainability so as to fulfil SDG Goal #2 (Zero Hunger) of the United Nations. Therefore, rather than setting up agricultural infrastructure, the objective was to address food sustainability problems by establishing micro farms in the city. It could be argued that collectively the volunteers, education facilities, communities, and NGO organizations could assist the people in acquiring more information about sustainable food, thus allowing them to actively participate in their community.

One of the deliverables during the project was the creation of social media awareness by posting posters about nutrition, food sustainability in cities, and Zero Hunger using the Instagram site. The other deliverable involved participating in an online seminar involving approximately thirty people to discuss the issue of food insecurity and propose micro-farm alternatives. Pre and post-surveys were conducted to measure knowledge levels. Finally, the researchers created a prototype wiring schematic of a harvest distribution app to show how the proposed food distribution system should operate. The five key steps of the PMBOK include initiating, planning, execution, monitoring, and closure of the approach. In addition, the scope, schedule, quality, resource management, communications, risk, and stakeholder management were taken into account.

2.0 Scope, Objectives and Completion Criteria

2.1 Project Objectives

GrowTogether project aims to contribute towards United Nations SDG Goal 2: Zero Hunger by creating awareness amongst B40 household about urban food insecurity. Objectives for the project were created during the initiation phase, and further other phases each goal is broken down into measurable deliverables that will be achieved within the fourteen weeks of implementation.

The first objective is for GrowTogether project to create and publish content regarding awareness on urban food insecurity, sustainable practices, and urban micro-farm. A minimum

number of posters and promotional posts must be created to ensure continued engagement in the process.

The second objective involves hosting and conducting an awareness webinar. During the seminar, topics related to food insecurity and urban micro-farms would be discussed. In addition to that, awareness level of the attendees can also be increased through live presentations and interactions.

The third objective is to develop wireframe prototypes that demonstrate the system design for collecting and distributing crops grown at urban micro-farm.

Lastly, the fourth objective entails conducting surveys to evaluate changes in awareness level of the audience before and after the seminar.



Figure 1: Webinar Poster

Webinar poster is designed as a main promotional material to announce Zero Hunger awareness webinar. It clearly presents the webinar topic, invited speaker, session date and time, platform and discussion topics by helping to attract participants and communicate the educational purpose of events.




Figure 2: Pre-Webinar Survey Screenshots

This screenshot shows the pre-webinar survey responses collected before the webinar session. The survey was used to assess participant initial level of awareness regarding food insecurity, urban faming, and sustainability food solutions before the webinar session was conducted.

2.2 Acceptance Criteria

Completion of tasks was determined by the verification process involving the matching of each work package with deliverables specified in the Work Breakdown Structure and Project Plan schedule. All critical deliverables were delivered within the planned project period.

Delivery of the webinar was made possible with participation by participants during the course of educating them with regard to urban food insecurity and micro-farms sustainability. During this process, discussions and explanations of the projects were made by members of the project.

Social Media marketing was achieved through the posting of awareness-related educational poster designs, infographic designs, webinars and engagements on the project Instagram page. Interaction through likes, comments and sharing by the audience was evidence of success in communicating through social media.

Wireframe Prototype was developed as a system that demonstrated the idea of the flow process of harvest-distribution for urban micro-farming support. While non-operational, the wireframe served as an educational awareness technology demonstration as required.

Pre-survey analysis and post-survey analysis showed increased knowledge among participants following the delivery of the webinar.




Figure 3: Instagram Poster

The above screenshot shows one of the educational campaign posters uploaded on Instagram. The visible likes, comments and audience integration indicate successful public engagement and shows that the content reached the intended audience effectively.




Figure 4: Instagram Campaign Grid

The Instagram campaign grid shows the full collection of campaign content developed during project execution. It reflects consistency in visual design, topic delivery and campaign branding throughout the social media awareness campaign.




Figure 5: Wireframe Prototype- Marketplace Screen

This wireframe shows the conceptual marketplace feature of the proposed GrowTogether application, where users can browse and purchase fresh produce from community micro-farms.




Figure 6: Wireframe Prototype – Community Map

This screenshot demonstrates the location-based feature where users can identify nearby farming activity points and community growing areas through map integration.




Figure 7: Wireframe Prototype – Volunteer Module

This interface present the volunteer management section, allowing users to connect with active community volunteers and participate in urban farming activities.




Figure 8: Wireframe Prototype – Monitoring Feature

This screenshot shows the crop monitoring function, where users can record weather condition and farming notes to support sustainable crop management.




Figure 9: Wireframe Prototype – Product Detail Screen

This interface demonstrates the products details section allowing users to review planting products and farming materials before adding them to the cart.

2.3 Evidence of Completion

The acceptance criteria formed the basis for defining when the goals of the project were met. The acceptance criteria were established in relation to the project's scope and requirements from its sponsor.

The project must have demonstrated:

- Completion of at least one webinar session successfully
- Publication of social media content consistently while executing the project
- Presentation of a working prototype through a wireframe during the evaluation phase
- Measurable increase in awareness through completion of both pre-survey and post-survey
- Finalization of the report and presentation based on deliverables

The acceptance criteria for the webinars were based on number of attendees and quality of education. Acceptance criteria for social media content were defined by interaction with the content like viewing, commenting, liking, and sharing.




Figure 10: Webinar Live Session Screenshot

This screenshot shows the webinar session during live delivery, where participants were guided to access the project Instagram page through QR code scanning for continued campaign engagement.

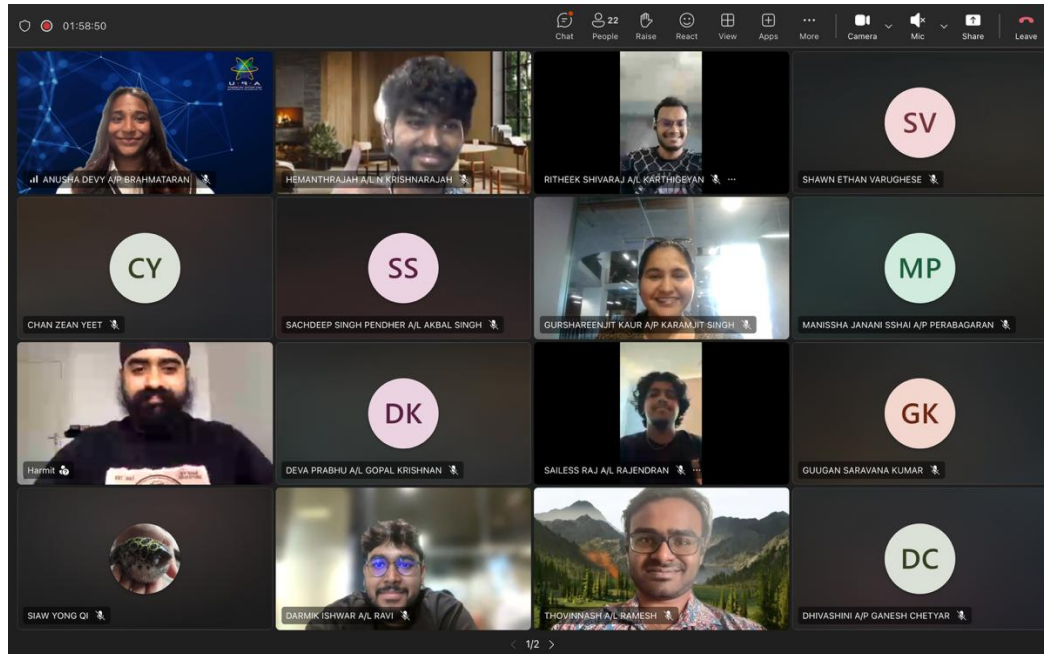


Figure 11: Webinar Closing Picture

This is the last point of the webinar, where the participants stayed until the end of the session since a group capture was to be made. It shows the attendance and participation rates during the event. The picture can be considered the witness of the successful completion and conduction of the webinar, where various participants were involved. It also shows the interactions of the audience and favours the success of the awareness exercise undertaken.

3.0 Evaluation of Quality Objective

3.1 Quality Objectives

Quality Objective	Target	Person-in-Charge
The social media awareness campaign shall achieve meaningful audience reach on the chosen platform.	Over 300 total engagements (likes + comments + shares) across all posts by Week 11	Social Media Team (Anusha Devy + Darmik)
The awareness webinar shall deliver educational value to the target audience on Zero Hunger and urban micro-farming.	More than 30 live attendees. Average post-webinar rating more than or equal to 4.0 on a 5-point scale.	Webinar Coordination Team (Adam Jerome + Sailess Raj)
Social media posts, webinar content and the prototype wireframe shall be understandable, accurate and relevant to the Zero Hunger objective.	More than or equal to 90% of content items pass editorial checklist before publication. Zero published items containing factual errors.	Project Manager (Gurshareenjit) + Assistant PM (Hemanthrajah)
The pre- and post-survey shall demonstrate a measurable improvement in audience awareness of urban food insecurity.	Increase of more than or equal to 20 percentage points between pre- and post-survey awareness score, with 30 or more valid responses in each survey.	Survey and Evaluation Team (Darsyen + Thovinaash)
All deliverables listed in the Scope Statement shall be completed within the 14-week academic semester baseline.	Schedule Performance Index (SPI) should be 0.95 or more at every Project Performance Report checkpoint.	Project Manager (Gurshareenjit)
Project documentation (charter, plan, WBS, reports) shall comply with the module marking guide.	100% of required report sections present with zero missing appendix items.	Assistant Project Manager (Hemanthrajah)

All identified risks shall be logged, analysed and assigned a response before they could impact the project.	100% of high-priority risks in the Risk Register have a named owner and a mitigation action recorded prior to the Executing phase.	Assistant Survey & Evaluation (Thovinnash)
--	--	--

Figure 12: Quality Objectives

3.2 Project and Product Quality Criteria

Project quality was assessed via criteria of scope, schedule, stakeholders, risk and team performance, tracked at the Project Performance Reports. Product quality was measured via deliverable-specific criteria. A content editorial check sheet and calendar, webinars attended and feedback scores, prototype walkthrough success rate versus the Requirements Traceability Matrix, sample size and statistical uplift for the surveys, report-conformance and similarity scores.

Before delivery, the team internally tested all assets, including social-media check sheets, prototype reviews and webinar dry-runs. Performance and stakeholder feedback verified the project was successful as the campaign reached its goal of 300 engagements, and webinars received positive feedback. Finally, survey scores confirmed the project raised awareness of urban food insecurity, and the project was archived.

The campaign has reached 843 accounts and the "It's More Than Farming" post has generated 789 views, driving awareness for the campaign. This visibility directly contributes to the goal of sharing educational material about sustainable urban micro-farming with a large audience.




Figure 13: Total Views Achieved in the social media account

The project gained 538 total engagements, mostly through posts (100%) and not stories. The high engagement on the "Thank You" posts suggests that attempts to enhance community and build appreciation among the 121 total followers were successful.




Figure 14: Total Interactions & Engagements

Engagement metrics show that **96.7% of interactions** came from existing followers, suggesting strong resonance with the core target audience. These **481 interactions** demonstrate the effectiveness of using consistent campaign visuals to maintain audience interest throughout the project lifecycle.




Figure 15: Engagement of Interactions

Over a recent 7-day period, the campaign reached **66 accounts**, with a "Thank You" post generating **151 views** from a highly engaged follower base of **88.2%**. This indicates steady progress in maintaining awareness levels even as the campaign moved toward its closing phase.





Figure 16: Total Accounts Reached

Within a two-week window, the campaign reached **444 accounts**, successfully balancing reach between **followers (68.4%)** and **non-followers (31.6%)**. The diversified content, ranging from farming facts to campaign updates, successfully attracted **1,708 total views**.

*Figure 17: Account reached between followers and non-followers*

Profile activity peaked at **226 actions**, including **224 profile visits**, showing that the content effectively drove users to seek more information about the GrowTogether initiative. The **623 total interactions** across various top-performing posts validate the objective of creating interactive and shareable social media content.




Figure 18: Peaked Interactions

4.0 Schedule Objectives

The project was scheduled to last 66 days from January 27, 2026, to April 28, 2026. The schedule was based on the five project lifecycle phases: Initiating, Planning, Executing, Monitoring & Controlling, and Closing. The project resulted in the deliverables of Project Charter (Week 5), Project Plan Presentation (Week 7) and Final Report (Week 12), as per the Sponsor's high-level requirements. Although there were slight deviations during the implementation of social media and webinar activities, the project schedule was on target for final submission and close-out in late April.

WBS	Task Name	Duration	Start	Finish	Predecessor	Resource Names
	PROJECT PLAN G4	66 days?	Tue 27/1/26	Tue 28/4/26		
	1 Phase 1: Initiating	30 days	Tue 27/1/26	Mon 9/3/26		
1.1	Form project team and appoint Project Manager	0.25 days	Tue 27/1/26	Tue 27/1/26		ALL MEMBERS
1.2	Project charter briefing with sponsors	0.25 days	Tue 27/1/26	Tue 27/1/26		DR. HEMA
1.3	Select and confirm relevant SDG	0.5 days	Tue 27/1/26	Wed 28/1/26	3,4	ALL MEMBERS
1.4	Research selected SDG and application relevance	0.38 days	Thu 29/1/26	Tue 3/2/26	5	ALL MEMBERS
1.5	Develop Project Charter	1.5 days	Tue 3/2/26	Sun 8/3/26	6	ALL MEMBERS
1.6	Review Project Charter progress with sponsors	0.38 days	Tue 3/3/26	Tue 3/3/26	7SS	ALL MEMBERS
1.7	Submit Project Charter	0.13 days	Mon 9/3/26	Mon 9/3/26	7	SHAREEN
	2 Phase 2: Planning	15 days	Tue 10/3/26	Mon 30/3/26		
2.1	Define Project Scope	1.38 days	Wed 11/3/26	Thu 12/3/26	9	HEMANTH,DARSYEN
2.2	Design Pre Survey Questions	0.38 days	Wed 11/3/26	Wed 11/3/26	9	DARSYEN
2.3	Develop content strategy and social media calendar	1.25 days	Mon 16/3/26	Tue 17/3/26	11	ANUSHA,DARMIK,SHAREEN
2.4	Search for speaker for webinar	2.88 days	Tue 10/3/26	Thu 12/3/26	9	ADAM,SHAREEN
2.5	Prepare Project Plan	7.5 days	Thu 12/3/26	Mon 23/3/26	11	ADAM,SHAREEN,HEMANTH,SAILESS
2.6	Create Gantt Chart	1 day	Wed 25/3/26	Thu 26/3/26	15SS	ADAM,SHAREEN,HEMANTH,SAILESS
2.7	Develop Work Breakdown Structure (WBS)	1 day	Wed 25/3/26	Wed 25/3/26	15SS	ADAM,HEMANTH,SAILESS,SHAREEN
2.8	Finalize scope statement	0.25 days	Fri 13/3/26	Fri 13/3/26	11	HEMANTH,DARSYEN
2.9	Project Schedule Management	3.13 days	Mon 16/3/26	Thu 19/3/26	18	ADAM,SHAREEN,HEMANTH,SAILESS
2.1	Set webinar date	0.25 days	Wed 18/3/26	Wed 18/3/26	14SS	ALL MEMBERS
2.11	Create Workload Matrix	2.25 days	Wed 25/3/26	Fri 27/3/26	15SS	ANUSHA,DARMIK,ADAM,HEMANTH,SAILESS
2.12	Prepare Project Plan Presentation	1.5 days	Thu 26/3/26	Fri 27/3/26	15,16,17,18	DARMIK,DARSYEN,THOVINNASH,ANUSHA
2.13	Submit Project Plan and Presentation Slide	1 day	Fri 27/3/26	Fri 27/3/26		SHAREEN
2.14	Presentation	1 day	Mon 30/3/26	Mon 30/3/26		SHAREEN
	3 Phase 3: Executing	33 days	Wed 11/3/26	Fri 24/4/26		
3.1	Conduct Pre-Survey	0.5 days	Fri 13/3/26	Fri 13/3/26	12	DARSYEN,THOVINNASH
3.2	Distribute Pre-Survey to Target Audience	0.38 days	Mon 16/3/26	Mon 16/3/26	26	ALL MEMBERS
3.3	Analyze Pre-Survey Data	1 day	Tue 17/3/26	Tue 17/3/26	27	HEMANTH
3.4	Set up GrowTogether social media account	1 day	Fri 20/3/26	Fri 20/3/26	13	SHAREEN
3.5	Build audience engagements	7 days	Mon 23/3/26	Tue 31/3/26	29	ADAM,DARSYEN,SAILESS,THOVINNASH,ANUSHA
3.6	Create social media designs	25 days	Fri 20/3/26	Thu 23/4/26	13	ANUSHA,DARMIK,SHAREEN
3.7	Write campaign content	1 day	Fri 20/3/26	Fri 20/3/26	13	ANUSHA,SHAREEN
3.8	Launch social media campaign	24 days	Mon 23/3/26	Thu 23/4/26	29,32	SHAREEN,ANUSHA
3.9	Produce promotional video	4 days	Mon 23/3/26	Thu 26/3/26	33SS	ANUSHA,DARMIK,SHAREEN
3.1	Share campaign contents on social media channels	0.13 days	Wed 18/3/26	Wed 18/3/26		ALL MEMBERS
3.11	Prepare Webinar Poster	4 days	Mon 23/3/26	Thu 26/3/26	14	ANUSHA,DARMIK,SHAREEN
3.12	Update social media posts	2 days	Thu 23/4/26	Fri 24/4/26	33	ANUSHA,DARMIK
3.13	Prepare webinar materials and team tasks	6 days	Thu 26/3/26	Thu 2/4/26	36	ADAM,SAILESS,ANUSHA,DARMIK
3.14	Conduct Webinar	0.25 days	Fri 3/4/26	Fri 3/4/26	14,38	ALL MEMBERS
3.15	Prepare Post-Survey	0.5 days	Wed 18/3/26	Wed 18/3/26	28	DARSYEN,THOVINNASH
3.16	Collect Post-Survey	0.5 days	Mon 6/4/26	Mon 6/4/26	39,40	DARSYEN,THOVINNASH
3.17	Analyze Post-Survey	0.38 days	Mon 6/4/26	Mon 6/4/26	41SS	DARSYEN,THOVINNASH
	4 Phase 4: Monitoring & Controlling	30 days	Wed 18/3/26	Tue 28/4/26		
4.1	Monitor engagement performance	25 days	Wed 18/3/26	Tue 21/4/26		ANUSHA,DARMIK
4.2	Review webinar outcomes with team and sponsors	11 days	Thu 19/3/26	Thu 2/4/26		ADAM,SAILESS
4.3	Adjust engagement strategies	8 days	Fri 3/4/26	Tue 14/4/26	44SS	HEMANTH,SHAREEN
4.4	Monitor project risks	0.38 days	Wed 15/4/26	Wed 15/4/26		DARSYEN,THOVINNASH

Figure 19: Schedule Objectives

4.5	Track team progress and deadlines	0.25 days	Mon 30/3/26	Mon 30/3/26	ALL MEMBERS
4.6	Evaluate project performance	0.25 days	Wed 29/4/26	Wed 29/4/26	ALL MEMBERS
5 Phase 5: Closing		20 days	Wed 1/4/26	Sun 26/4/27	
5.1	Conduct Final Project Review	0.38 days	Wed 29/4/26	Wed 29/4/26	49 ALL MEMBERS
5.2	Prepare post-webinar report	6 days	Fri 10/4/26	Fri 17/4/26	39,42 ADAM, SAILESS
5.3	Collect participant feedback	0.5 days	Mon 6/4/26	Mon 6/4/26	39 DARSYEN, THOVINNASH
5.4	Identify improvement areas on webinar	1 day	Mon 6/4/26	Mon 6/4/26	39 ADAM, SAILESS
5.5	Risk and Issue	1 day	Mon 6/4/26	Mon 6/4/26	39 ADAM, SAILESS
5.6	Risk Mitigation	1 day	Tue 7/4/26	Tue 7/4/26	55 ADAM, SAILESS
5.7	Risk Registry	1 day	Wed 8/4/26	Wed 8/4/26	56 ADAM, SAILESS
5.8	Risk Matrix	1 day	Thu 9/4/26	Thu 9/4/26	57 ADAM, SAILESS
5.9	Create Lesson Learnt Report	0.38 days	Mon 20/4/26	Mon 20/4/26	52,54 ALL MEMBERS
5.1	Deliver final presentation	0.13 days	Thu 23/4/26	Thu 23/4/26	59 ALL MEMBERS
5.11	Complete Final Project Report	0 days	Sat 25/4/26	Sat 25/4/26	ALL MEMBERS
5.12	Submit final report and presentation slides	2 days	Sun 26/4/26	Sun 26/4/27	62 HEMANTH, SHAREEN

Figure 20: Schedule Objectives (Continuation)

5.0 Summary of Final Project

The project's purpose, expressed in the business case, was to raise awareness of urban food insecurity among B40 communities through low-cost, technology-enabled outreach. Benefits realisation was measured against this purpose and against the acceptance criteria recorded in the Charter.

Three categories of benefit were achieved. First and foremost, is the awareness benefit in which the post-survey showed a measurable improvement regarding the audience knowledge of urban food insecurity issues when compared to the pre-survey baseline, which satisfied the project's underlying purpose. The questions about practical micro-farming options have a more stronger uplift, which suggests that the campaign successfully translated the SDG, which is an abstract concept, into a form of actionable awareness.

The second benefit is the social-media campaign. It should be noted that the social media campaign has successfully reached its goal, which is to reach or exceed the 300-engagement acceptance threshold, while the webinar exceeded the 30-attendee threshold. This has proven that the chosen channels have reached a meaningful audience for the cost.

Meanwhile the third and final benefit is the capability benefit. In this benefit is where the wireframe prototype produced a tangible artefact that future cohorts or external partners could extend into a working application, leaving an asset behind rather than only an event.

The team also has realised about the presence of the secondary benefits not explicitly required by the Charter. Despite that being an occurrence, it, however, has not been any formal issue or problem that could have been problematic towards the whole project. It instead has been thoroughly consistent with the PMBOK view that the projects have the purpose in delivering organisational values beyond their primary deliverables.

These include practical experience for ten students in applying PMBOK process groups end-to-end, a reusable set of project templates (charter, plan, risk register, performance report) that can be adapted by future tutorial groups, and a demonstrable contribution to APU's wider engagement with the United Nations Sustainable Development Goals.

All claimed benefits are evidenced in the appendices and in the analytics records retained in the project archive, ensuring transparent benefit verification rather than self-reported success. This evidence-led approach to benefits realisation also created a clear audit trail for the marking and review process and demonstrates that the project's outcomes are reproducible and defensible.

6.0 Summary of Risks and Issues

Risk management was carried out based on the PMBOK process, which includes planning risk management, identifying risks, analysing risks, planning responses, and monitoring them throughout the project. To keep everything organised, the team used a Risk Register in Appendix A2. This register recorded each risk together with its probability, impact, priority, response strategy, owner, and current status.

The team also used a probability and impact matrix to decide which risks needed the most attention. Any risk that had both high probability and high impact was treated as a Priority-1 risk. These risks required proper response planning before the project moved into the Executing phase, so that the team could reduce the chance of serious problems later.

One of the main risks was scope creep, where extra campaign content was informally suggested during the Executing phase. To manage this, the team used formal change control instead of accepting changes casually. As a result, one change request was raised, approved, and included in the project without changing the original scope baseline.

Another risk was resource over-allocation, as team members had other module deadlines at the same time. This could have affected their ability to complete project tasks on time. To reduce this risk, the team used resource leveling in the Gantt chart and prepared a RACI matrix that included a backup responsible person for every important task. Because of this, no critical task was stopped or delayed.

The team also faced the risk of a schedule slip on the critical path, which could have affected the Week 11 webinar deadline. To manage this, the team monitored the Schedule Performance Index during every performance report. Fast-tracking was also prepared as a backup plan if needed. In the end, the project stayed on track, with the SPI remaining at 0.95 or above and ending with a final SPI of 0.98.

Another important risk was low webinar attendance, which could have affected stakeholder engagement. The team responded by using pre-registration, promoting the event through multiple campaign posts, and sending reminder messages 24 hours before the webinar. These actions helped the team meet the expected attendance target.

The final major risk was misinformation or poor-quality content, especially when sharing information about Zero Hunger. To prevent this, the team used an editorial checklist, verified sources, and carried out peer reviews before publishing any content. This helped ensure that the information shared was accurate, and no factual errors were recorded.

6.2 Issues Encountered

Two issues happened during the project and were recorded in the Issue Log. The first issue was unclear wording in three pre-survey questions, which was discovered during peer review in Week 6. The team corrected the questions before releasing the survey and introduced a two-person peer review rule for future materials, including the post-survey.

The second issue was a short platform connectivity problem during the webinar dry run. Since it was identified before the actual event, the team was able to solve it by changing the host machine. A backup host was also added as part of the standard procedure for the live webinar. This helped reduce the chance of the same problem happening during the real session.

All risks and issues were reviewed during the weekly stand-up meetings and included in the Project Performance Reports. By recording both major risks and smaller issues clearly, the team was able to show transparency and proper control throughout the project. This also

showed that the Risk Register and Issue Log were actively used to support decision-making, rather than being treated only as documents for submission.

7.0 Lessons Learned Summary

We collected lessons learned throughout the project life cycle. The team was asked to note successes and challenges in each Project Performance Report and a final Lessons Learned meeting was conducted at Week 12 close-out. The complete Lessons Learned Report is in Appendix A4; the highlights are below.

8.0 Project Assessment

The GrowTogether project was a successful project because it met the project's primary goal of increasing awareness of SDG 2: Zero Hunger, particularly urban food insecurity faced by the B40 in Malaysia. The project was able to showcase micro-farming as a community solution through the integration of social media, webinar, survey results and an idea for a mobile application for tracking harvests and food distribution.

The project was very successful in its Instagram awareness campaign. This campaign received more engagement than anticipated (761 engagements vs 300). This shows that the campaign materials were successful in engaging the audience. The Instagram account also performed well with the audience, with good engagement, views, profile views and followers, which indicates that the awareness campaign materials were relevant and interesting.

The webinar also helped to achieve the project goals by raising awareness about Zero Hunger, food insecurity, urban farming, food systems and potential community solutions. The team was able to assess audience learning and gather feedback through the webinar and surveys, which assisted in measuring the success of the awareness campaign.

The GrowTogether project was managed to the five phases of projects - initiate, plan, execute, monitor and control, and close. Project management tools, including the project schedule, Work Breakdown Structure (WBS), workload matrix, surveys, performance monitoring and risk

management were used to support the project activities. They were used to align tasks, monitor work, and manage issues and risks.

There were limited resources for the project (time, team collaboration, audience engagement) but the team overcame these by communicating, tracking work and embracing change. This helped meet project deliverables and ensure the project was on schedule to meet its goals.

In conclusion, the GrowTogether project demonstrated project management processes for developing and delivering an awareness campaign. This project increased awareness of food insecurity and sustainable food choices and exposed the team to other important skill development in teamwork, communication, planning, problem solving and documentation. To improve future campaigns, the team could promote earlier, involve the audience more and further develop the mobile app concept to improve the success of the solution.

9.0 Appendix

PRMGT Project Plan

PROJECT SCOPE STATEMENT

Project Title: ~~GrowTogether~~

Tutorial & Group: T2-G4

Product Scope Description:

The ~~GrowTogether~~ project product scope is developed progressively with the help of the project description and requirements provided in Project Charter. The project aims at creating an awareness program that will target urban food insecurity among the B40 families per the United Nations Sustainable Development Goal 2: Zero Hunger.

It consists of development of social media campaign, awareness webinars and prototype conceptual applications. The proposed solution encourages micro-farming in the communities through the use of the unutilized urban areas and the production of sustainable food products. The areas covered are also educational content creation, involvement of stakeholders as well as the fundamental concepts of data tracking which pertain to food insecurity and engagement.

Project Deliverables:

Project deliverables are gradually expanded upon to the project description, product characteristics and requirements outlined in Project Charter. The essential deliverables will be:

- Project Charter which presents the objectives, scope, risks and stakeholders.
- Social media campaign tools like infographics, posts, promotional content.
- Wireframe/mockup Conceptual application prototype that tracks harvest distribution and participation.
- Survey result data on the measure of awareness improvement.

Project Acceptance Criteria:

The acceptance criteria are the guidelines that should be satisfied so that the stakeholders accept the project deliverables. The project will be said to be successful when:

- Minimum anticipated engagements reached through the social media campaign is 300 (likes, comments, shares).
- The awareness webinar will ensure at least 30 people take part, plus the results of the survey will show better awareness of the subject of urban food insecurity.
- The deliverables (posts, webinar content, and prototype) are understandable, appropriate, and relevant to the Zero Hunger objective.
- The final report and presentation are fair and truthful regarding the execution of the project, its results, and analysis.

Project Exclusions:

Project exclusions are an explicit statement of what the ~~GrowTogether~~ project will not feature in its scope. These include:

- Creation of a working mobile or web app.
- Welfare system (government), grocery system, or financial system integration.
- Massive adoption of micro-farm infrastructure.
- Paid social media advertising, influencer collaborations or long-term campaign management.

Project Constraints:

Scope

PROJECT SCOPE STATEMENT

Project Title: ~~Grow Together~~

Tutorial & Group: T2-G4

The project is constrained by a number of factors that can affect the project:

- **Time Constraint:** The project has to be done in the 14-week academic semester.
- **Financial constraint:** Little or no financial means to implement physically, to advertise, to have more sophisticated equipment.
- **Resource Constraint:** Reliance on student team members and voluntary participation.
- **Limitations on technology:** The use of rudimentary tools, including social media, survey tools, and design software.

Project Assumptions:

The available assumptions are taken to be true, in terms of planning, but not necessarily entirely true:

- At minimum, 30 people will be present in the awareness webinar.
- The target audience will be exposed to social media content and attain the necessary engagement metrics.
- The participants are ready to give feedback in the form of surveys and communication in social media.
- The project team will be able to create and release the intended campaign contents within the schedule.

Project Schedule and Gantt Chart

WBS	Task Name	Duration	Start	Finish	Predecessor	Resource Names
PROJECT PLAN G4		66 days?	Tue 27/1/26	Tue 28/4/26		
1 Phase 1: Initiating		30 days	Tue 27/1/26	Mon 9/3/26		
1.1	Form project team and appoint Project Manager	0.25 days	Tue 27/1/26	Tue 27/1/26		ALL MEMBERS
1.2	Project charter briefing with sponsors	0.25 days	Tue 27/1/26	Tue 27/1/26		DR. HEMA
1.3	Select and confirm relevant SDG	0.5 days	Tue 27/1/26	Wed 28/1/26	3,4	ALL MEMBERS
1.4	Research selected SDG and application relevance	0.38 days	Thu 29/1/26	Tue 3/2/26	5	ALL MEMBERS
1.5	Develop Project Charter	1.5 days	Tue 3/2/26	Sun 8/3/26	6	ALL MEMBERS
1.6	Review Project Charter progress with sponsors	0.38 days	Tue 3/3/26	Tue 3/3/26	7SS	ALL MEMBERS
1.7	Submit Project Charter	0.13 days	Mon 9/3/26	Mon 9/3/26	7	SHAREEN
2 Phase 2: Planning		15 days	Tue 10/3/26	Mon 30/3/26		
2.1	Define Project Scope	1.38 days	Wed 11/3/26	Thu 12/3/26	9	HEMANTH,DARSYEN
2.2	Design Pre Survey Questions	0.38 days	Wed 11/3/26	Wed 11/3/26	9	DARSYEN
2.3	Develop content strategy and social media calendar	1.25 days	Mon 16/3/26	Tue 17/3/26	11	ANUSHA,DARMIK,SHAREEN
2.4	Search for speaker for webinar	2.88 days	Tue 10/3/26	Thu 12/3/26	9	ADAM,SHAREEN
2.5	Prepare Project Plan	7.5 days	Thu 12/3/26	Mon 23/3/26	11	ADAM,SHAREEN,HEMANTH,SAILESS
2.6	Create Gantt Chart	1 day	Wed 25/3/26	Thu 26/3/26	15SS	ADAM,SHAREEN,HEMANTH,SAILESS
2.7	Develop Work Breakdown Structure (WBS)	1 day	Wed 25/3/26	Wed 25/3/26	15SS	ADAM,HEMANTH,SAILESS,SHAREEN
2.8	Finalize scope statement	0.25 days	Fri 13/3/26	Fri 13/3/26	11	HEMANTH,DARSYEN
2.9	Project Schedule Management	3.13 days	Mon 16/3/26	Thu 19/3/26	18	ADAM,SHAREEN,HEMANTH,SAILESS
2.1	Set webinar date	0.25 days	Wed 18/3/26	Wed 18/3/26	14SS	ALL MEMBERS
2.11	Create Workload Matrix	2.25 days	Wed 25/3/26	Fri 27/3/26	15SS	ANUSHA,DARMIK,ADAM,HEMANTH,SAILESS
2.12	Prepare Project Plan Presentation	1.5 days	Thu 26/3/26	Fri 27/3/26	15,16,17,18	DARMIK,DARSYEN,THOVINNASH,ANUSHA
2.13	Submit Project Plan and Presentation Slide	1 day	Fri 27/3/26	Fri 27/3/26		SHAREEN
2.14	Presentation	1 day	Mon 30/3/26	Mon 30/3/26		SHAREEN
3 Phase 3: Executing		33 days	Wed 11/3/26	Fri 24/4/26		
3.1	Conduct Pre-Survey	0.5 days	Fri 13/3/26	Fri 13/3/26	12	DARSYEN,THOVINNASH
3.2	Distribute Pre-Survey to Target Audience	0.38 days	Mon 16/3/26	Mon 16/3/26	26	ALL MEMBERS
3.3	Analyze Pre-Survey Data	1 day	Tue 17/3/26	Tue 17/3/26	27	HEMANTH
3.4	Set up GrowTogether social media account	1 day	Fri 20/3/26	Fri 20/3/26	13	SHAREEN
3.5	Build audience engagements	7 days	Mon 23/3/26	Tue 31/3/26	29	ADAM,DARSYEN,SAILESS,THOVINNASH,ANUSHA
3.6	Create social media designs	25 days	Fri 20/3/26	Thu 23/4/26	13	ANUSHA,DARMIK,SHAREEN
3.7	Write campaign content	1 day	Fri 20/3/26	Fri 20/3/26	13	ANUSHA,SHAREEN
3.8	Launch social media campaign	24 days	Mon 23/3/26	Thu 23/4/26	29,32	SHAREEN,ANUSHA
3.9	Produce promotional video	4 days	Mon 23/3/26	Thu 26/3/26	33SS	ANUSHA,DARMIK,SHAREEN
3.1	Share campaign contents on social media channels	0.13 days	Wed 18/3/26	Wed 18/3/26		ALL MEMBERS
3.11	Prepare Webinar Poster	4 days	Mon 23/3/26	Thu 26/3/26	14	ANUSHA,DARMIK,SHAREEN
3.12	Update social media posts	2 days	Thu 23/4/26	Fri 24/4/26	33	ANUSHA,DARMIK
3.13	Prepare webinar materials and team tasks	6 days	Thu 26/3/26	Thu 2/4/26	36	ADAM,SAILESS,ANUSHA,DARMIK
3.14	Conduct Webinar	0.25 days	Fri 3/4/26	Fri 3/4/26	14,38	ALL MEMBERS
3.15	Prepare Post-Survey	0.5 days	Wed 18/3/26	Wed 18/3/26	28	DARSYEN,THOVINNASH
3.16	Collect Post-Survey	0.5 days	Mon 6/4/26	Mon 6/4/26	39,40	DARSYEN,THOVINNASH
3.17	Analyze Post-Survey	0.38 days	Mon 6/4/26	Mon 6/4/26	41SS	DARSYEN,THOVINNASH
4 Phase 4: Monitoring & Controlling		30 days	Wed 18/3/26	Tue 28/4/26		
4.1	Monitor engagement performance	25 days	Wed 18/3/26	Tue 21/4/26		ANUSHA,DARMIK
4.2	Review webinar outcomes with team and sponsors	11 days	Thu 19/3/26	Thu 2/4/26		ADAM,SAILESS
4.3	Adjust engagement strategies	8 days	Fri 3/4/26	Tue 14/4/26	44SS	HEMANTH,SHAREEN
4.4	Monitor project risks	0.38 days	Wed 15/4/26	Wed 15/4/26		DARSYEN,THOVINNASH


4.5	Track team progress and deadlines	0.25 days	Mon 30/3/26	Mon 30/3/26		ALL MEMBERS
4.6	Evaluate project performance	0.25 days	Wed 29/4/26	Wed 29/4/26		ALL MEMBERS
5 Phase 5: Closing		20 days	Wed 1/4/26	Sun 26/4/27		
5.1	Conduct Final Project Review	0.38 days	Wed 29/4/26	Wed 29/4/26	49	ALL MEMBERS
5.2	Prepare post-webinar report	6 days	Fri 10/4/26	Fri 17/4/26	39,42	ADAM,SAILESS
5.3	Collect participant feedback	0.5 days	Mon 6/4/26	Mon 6/4/26	39	DARSYEN,THOVINNASH
5.4	Identify improvement areas on webinar	1 day	Mon 6/4/26	Mon 6/4/26	39	ADAM,SAILESS
5.5	Risk and Issue	1 day	Mon 6/4/26	Mon 6/4/26	39	ADAM,SAILESS
5.6	Risk Mitigation	1 day	Tue 7/4/26	Tue 7/4/26	55	ADAM,SAILESS
5.7	Risk Registry	1 day	Wed 8/4/26	Wed 8/4/26	56	ADAM,SAILESS
5.8	Risk Matrix	1 day	Thu 9/4/26	Thu 9/4/26	57	ADAM,SAILESS
5.9	Create Lesson Learnt Report	0.38 days	Mon 20/4/26	Mon 20/4/26	52,54	ALL MEMBERS
5.1	Deliver final presentation	0.13 days	Thu 23/4/26	Thu 23/4/26	59	ALL MEMBERS
5.11	Complete Final Project Report	0 days	Sat 25/4/26	Sat 25/4/26		ALL MEMBERS
5.12	Submit final report and presentation slides	2 days	Sun 26/4/26	Sun 26/4/27	62	HEMANTH,SHAREEN

Workload Matrix

NO.	STUDENT NAME	ID	ROLES & RESPONSIBILITIES
1.	Gurshareenjit Kaur	TP070385	Tasks: Project Manager, Webinar Emcee Documentation: Background, Objectives, Project Resources, Prepare project plan, Create Gantt Chart, Develop Work Breakdown Structure (WBS), Create Social Media Designs, Write Campaign Content, Prepare Webinar Poster, Deliver Final Presentation, Complete Final Project Report
2.	Hemanthrajah	TP070844	Tasks: Assistant Project Manager, Webinar Emcee Documentation: Scope, Prepare project plan, Create Gantt Chart, Develop Work Breakdown Structure(WBS), Deliver final presentation, Complete Final Project Report
3.	Anusha Devy	TP071154	Tasks: Social Media Manager Documentation: Assumptions, Create Workload Matrix, Prepare Project plan Presentation, Create Social Media Designs, Write Campaign Content, Prepare Webinar Poster, Prepare webinar materials and team tasks, Monitor engagement performance, Deliver final presentation , Complete Final Project Report
4.	Darmik Ishwar	TP070071	Tasks: Assistant Social Media Manager Documentation: Create Workload Matrix, Prepare Project plan Presentation, Create Social Media Designs, Prepare Webinar Poster, Prepare webinar materials and team tasks, Monitor engagement performance, Deliver final presentation , Complete Final Project Report
5.	Adam Jerome Joseph	TP071194	Tasks: Webinar Coordination Head Documentation: Deliverables, Prepare project plan, Create Gantt Chart, Develop Work Breakdown Structure(WBS), Prepare webinar materials and team tasks, Review webinar outcomes with team and sponsors, Prepare Post Webinar Report, Deliver final presentation , Complete Final Project Report

6.	Sailess Raj	TP070996	Tasks: Assistant Social Media Manager Documentation: Deliverables, Prepare project plan, Create Gantt Chart, Develop Work Breakdown Structure (WBS), Prepare webinar materials and team tasks, Review webinar outcomes with team and sponsors, Prepare Post Webinar Report, Deliver final presentation, Complete Final Project Report
7.	Darsyen	TP070635	Tasks: Survey and Evaluation Head Documentation: Scope, Prepare Project plan Presentation, Conduct Pre-Survey, Prepare Post-Survey, Collect and Analyze Post-Survey, Monitor project risks, Collect participant Feedback, Deliver final presentation, Complete Final Project Report
8.	Thovinnash	TP071046	Tasks: Assistant Survey and Evaluation Head Documentation: Risk analysis, Prepare Project plan Presentation, Conduct Pre-Survey, Prepare Post-Survey, Collect and Analyze Post-Survey, Monitor project risks, Collect participant Feedback, Deliver final presentation, Complete Final Project Report
9.	Ahmed	TP078596	Tasks: Logistics Documentation: Major milestone, Prepare Project plan Presentation, Deliver final presentation, Complete Final Project Report

Work Breakdown Structure

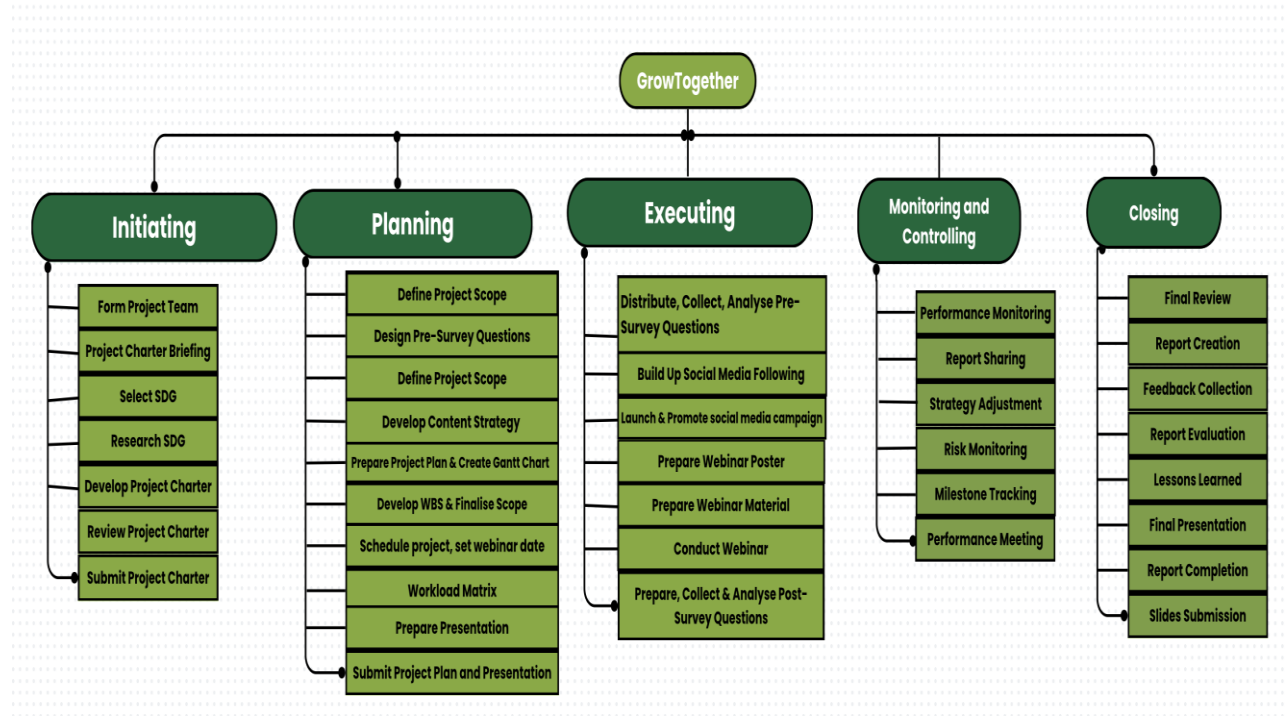

Risk Register

Risk Register

Risk ID	Risk Description	Likelihood	Impact	Severity (Likelihood × Impact)	Mitigation Strategies
1	Misinterpretation of campaign message	Medium	High	High	Use clear and simple language in all campaign materials. Ask peers or target audience members to review the message before publishing.
2	Low social media engagement	Medium	Medium	Medium	Post attractive visuals, use short captions, upload during peak hours, and encourage likes, shares, and comments.
3	Poor communication among team members	High	High	High	Hold frequent meetings and create a WhatsApp group for quick updates, discussions, and reminders.
4	Different schedules among team members	High	High	High	Prepare a clear timeline early, divide tasks properly, and set internal deadlines before the actual submission date.
5	Technical problems during webinar or presentation	Medium	High	High	Conduct a full technical test before the event, prepare backup devices, and assign a backup host in case of connection issues.

Risk Register

Risk ID	Risk Description	Likelihood	Impact	Severity (Likelihood × Impact)	Mitigation Strategies
6	Low attendance during webinar or event	Medium	High	High	Promote the event earlier, use reminder messages, and encourage pre-registration to estimate attendance more accurately.
7	Inaccurate or misleading information shared	Low	High	Medium	Check all facts carefully, use reliable sources, and ask team members to review the content before posting or presenting.
8	Unbalanced survey responses / sampling bias	Medium	High	High	Distribute the survey to a wider audience, especially the target group, and compare responses from different participant categories.
9	Lack of community participation in the micro-farm project	Medium	High	High	Conduct awareness sessions, explain the benefits clearly, and provide simple guidance so participants feel confident to join.
10	Negative feedback or criticism from the audience	Medium	Medium	Medium	Respond professionally, clarify misunderstandings politely, and use feedback to improve the project.

Quality Matrix

Deliverable	Quality Objective	Metric	Acceptance Target	Measurement Method	V&V Activity
Project Charter	Charter must give clear direction to all stakeholders.	% of required template sections completed.	100% (all 9 sections present).	Template checklist review.	Verification: peer review. Validation: Sponsor sign-off (Week 5).
Project Plan (WBS, Gantt, Workload Matrix)	Plan must cover full scope, schedule and responsibilities.	% of WBS work packages mapped to a Gantt task and an owner.	100% mapping (no orphan tasks).	Cross-check WBS ↔ Gantt ↔ Workload Matrix.	Verification: inspection by PM. Validation: Week 7 plan presentation.
Social Media Posts & Infographics	Content must be accurate, clear and on message.	Total audience engagement on the campaign.	≥ 300 engagements (likes + comments + shares) by Week 11.	Native platform analytics dashboard.	Verification: editorial check sheet. Validation: live engagement metrics.
Published Content (Accuracy)	No misinformation about Zero Hunger published.	Number of factual errors found after publication.	Zero published factual errors.	Source-verification log + peer review.	Verification: two-eye peer review before posting.

Deliverable	Quality Objective	Metric	Acceptance Target	Measurement Method	V&V Activity
Awareness Webinar (Reach)	Webinar must reach the planned audience size.	Number of live attendees.	≥ 30 live attendees (per Charter assumption) .	Webinar platform attendance log.	Validation: attendance record + screenshots.
Awareness Webinar (Quality)	Webinar must deliver clear, useful content.	Average post-webinar feedback rating.	Mean rating $\geq 4.0 / 5$.	Post-webinar feedback survey (Google Forms).	Validation: participant feedback.

Prototype Wireframe (Harvest-Distribution App)	Prototype must demonstrate all key user journeys.	% of stated requirements covered in the wireframe.	100% coverage of core journeys.	Walkthrough vs Requirements Traceability Matrix.	Verification: peer walkthrough. Validation: Sponsor review.
Pre- & Post-Survey (Awareness Uplift)	Project must measurably improve audience awareness.	Difference between pre- and post-survey awareness scores.	≥ 20 percentage-point uplift; ≥ 30 valid responses each survey.	Statistical comparison of paired survey results.	Validation: post-survey results.
Project Schedule (Process)	Project must stay on the baseline schedule.	Schedule Performance Index (SPI = EV / PV).	SPI ≥ 0.95 at every checkpoint.	Earned Value tracking on Gantt.	Verification: Project Performance Reports.
Final Project Report	Report must conform to module structure and academic integrity.	% of required sections + Turnitin similarity score.	100% sections; similarity $\leq 15\%$; word count 2,500–3,000.	Report checklist + Turnitin report.	Verification: section-by-section inspection. Validation: Sponsor acceptance Week 12.
